

VEGETATIVE PLAN (SEE DETAILS, SHEET C-3.7)			
SEEDS FOR GRASSED AREAS USE THE FOLLOWING MIXTURES.			
<u>MULCHING</u> RATE = 2 1/2 T/AC.	<div style="border: 1px solid black; padding: 5px; display: inline-block;">Ds1</div>	<u>PERMANENT</u>	<div style="border: 1px solid black; padding: 5px; display: inline-block;">Ds4</div>
<u>TEMPORARY</u> SEED WITH BAHIA 1.4 LB. / 1000 SQ. FT. APPLY AS NEEDED. BETWEEN JULY AND AUGUST SEED WITH RYEGRASS OTHERWISE 0.9 LB. / 1000 SQ. FT.	<div style="border: 1px solid black; padding: 5px; display: inline-block;">Ds2</div>	SOD  1ST YR FERTILIZER  LIME	BERMUDA  1500 LB./AC. 6-12-12  4000 LB./ACRE

**HAZARDOUS MATERIALS NOTE:**  
CONTRACTOR SHALL FOLLOW THE PRODUCT SPECIFIC PRACTICES WHEN HANDLING THE MATERIALS LISTED BELOW TO MINIMIZE IN STORM WATER DISCHARGE.

Product Specific Practices


**Petroleum Based Products** – Containers for products such as fuels, lubricants, and tars will be inspected daily for leaks and spills. This includes online vehicles such as machinery daily inspections and regular preventive maintenance of such equipment. Equipment maintenance areas will be located away from storm water drainage lines. In addition, temporary fueling lines will have a secondary containment liner to prevent/minimize site contamination. Discharge of oils, fuels, and lubricants is prohibited. Proper disposal methods will include collection in a suitable container and disposal as required by local and State regulations.

**Paints/Finishes/Solvents** – All products will be stored in tightly sealed original containers when not in use. These materials will not be discharged to the storm water collection system. Excess product, materials used with these products, and product containers will be disposed of according to manufacturer's specifications and recommendations.

**Concrete Truck Washing** – NO concrete trucks will be allowed to wash out or discharge surplus concrete or drum wash water onsite.

**Fertilizer/Herbicides** – These products will be applied at rates that do not exceed the manufacturer's specifications or above the guidelines set forth in the crop establishment or in the GSWQC Manual for Erosion and Sediment Control in Georgia. Any storage of these materials will be under cover in sealed containers.

**Building Materials** – No building or construction materials will be buried or disposed of onsite. All such material will be disposed of in proper waste disposal procedures.

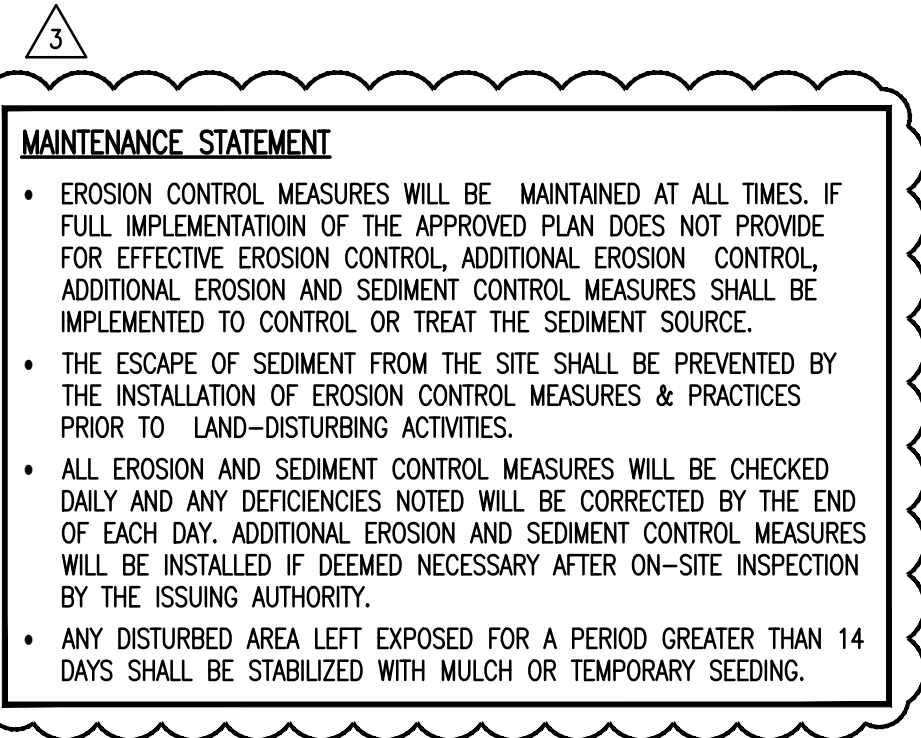

ANY DISTURBED AREA LEFT EXPOSED FOR A PERIOD GREATER THAN 14 DAYS SHALL BE STABILIZED WITH MULCH OR TEMPORARY SEEDING.

